

## Staff Report

**To:** Board of Directors  
**From:** Frank Kuhl  
**Date:** March 26, 2026

---

### **Agenda Item:** 4.2 Transfer Center Renovation Update

#### **Attachments:**

- 4.2.1 – 7 Construction Photos

#### **Recommendation:**

Informational item – Discussion only.

#### **Discussion:**

##### **Overall Status Summary**

The transfer center renovation continues to make good progress toward an early April finish.

During the last two weeks, the lobby has been closed to the public for flooring work, and will reopen on Saturday, March 21. While this closure presented some small hurdles, it caused no major disruptions or issues. Nine temporary bathroom units were placed outside to account for the closed public bathrooms.

##### **Work Completed Since Last Update**

Since last month's update, the most significant development has been the installation of polished concrete flooring in the lobby that is nearing completion. In addition, data cables have been pulled, and plumbing in the new bathroom and kitchen is complete.

##### **Current Construction Activities**

- The lobby flooring will be completed by Friday, March 20.
- Painting work is concluding.
- The dishwasher has been installed.




**Decisions or Board Actions Requested**

No board action is required at this time.

**Next Steps**

- Ceiling tiles will be installed during the week of March 23.
- Carpet should be installed during the week of April 6.



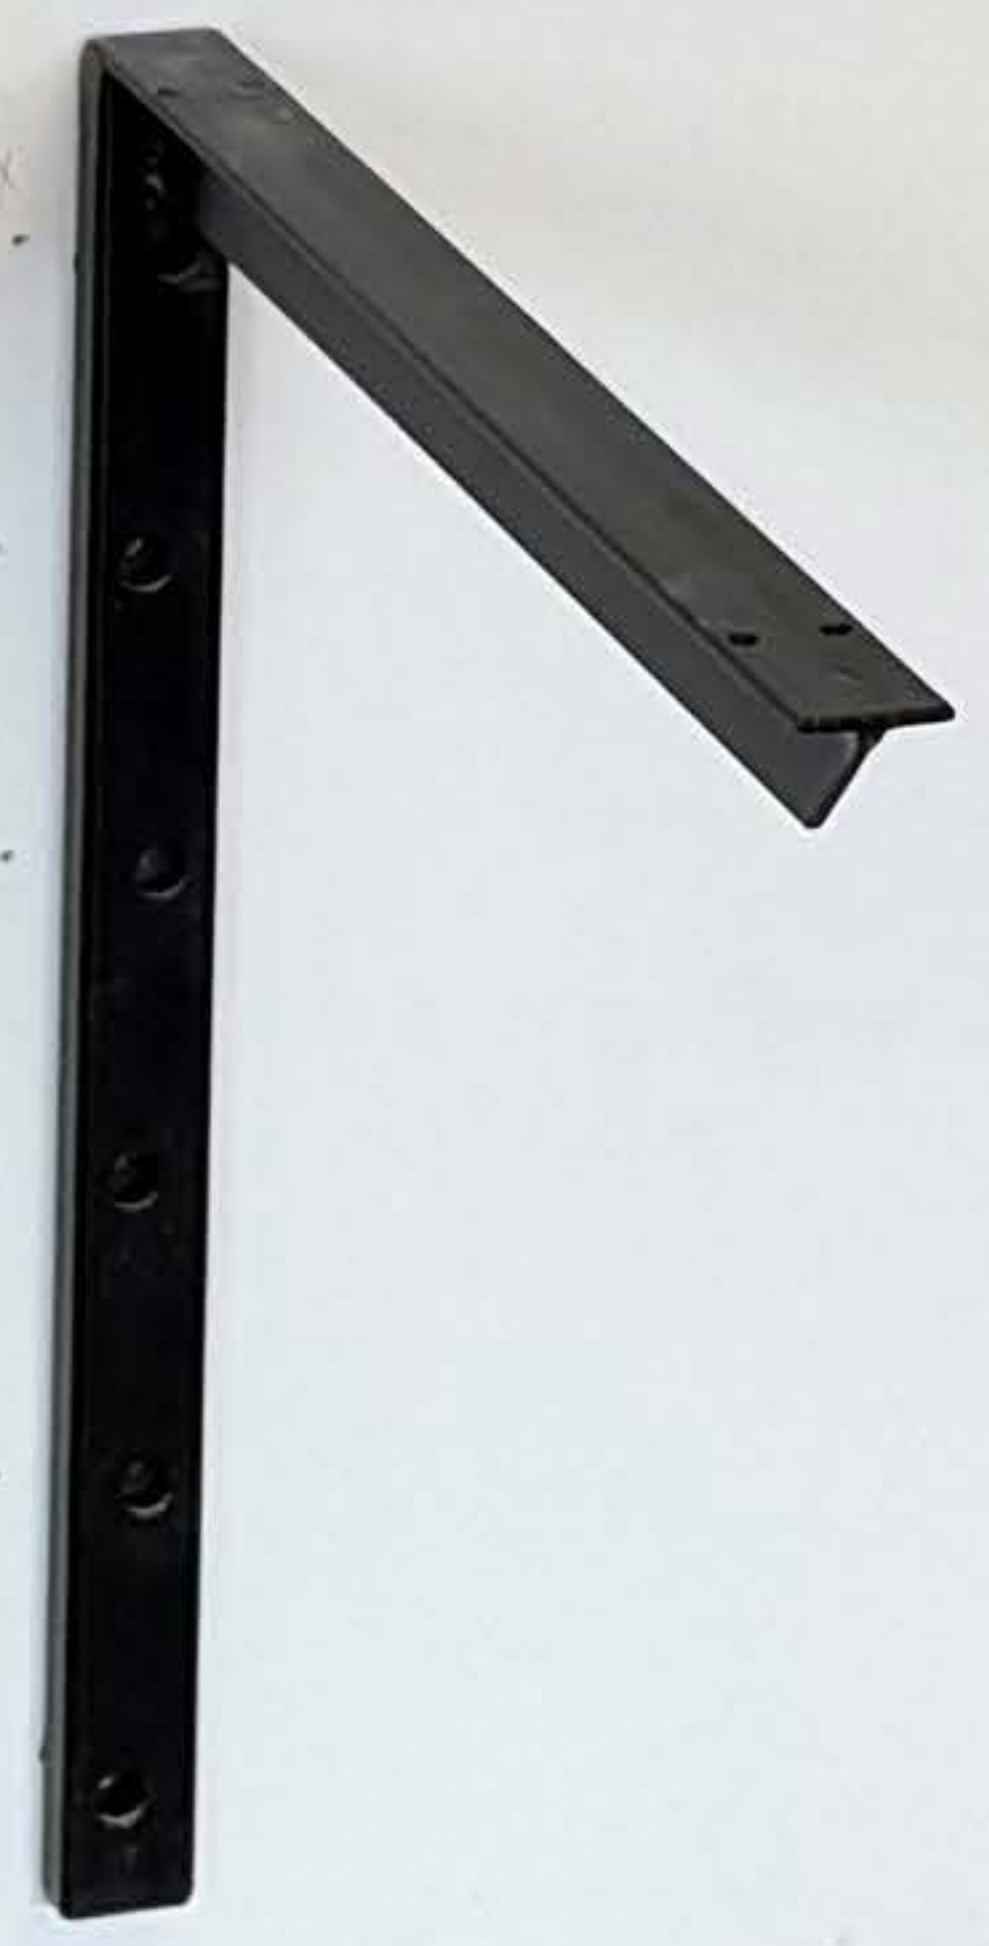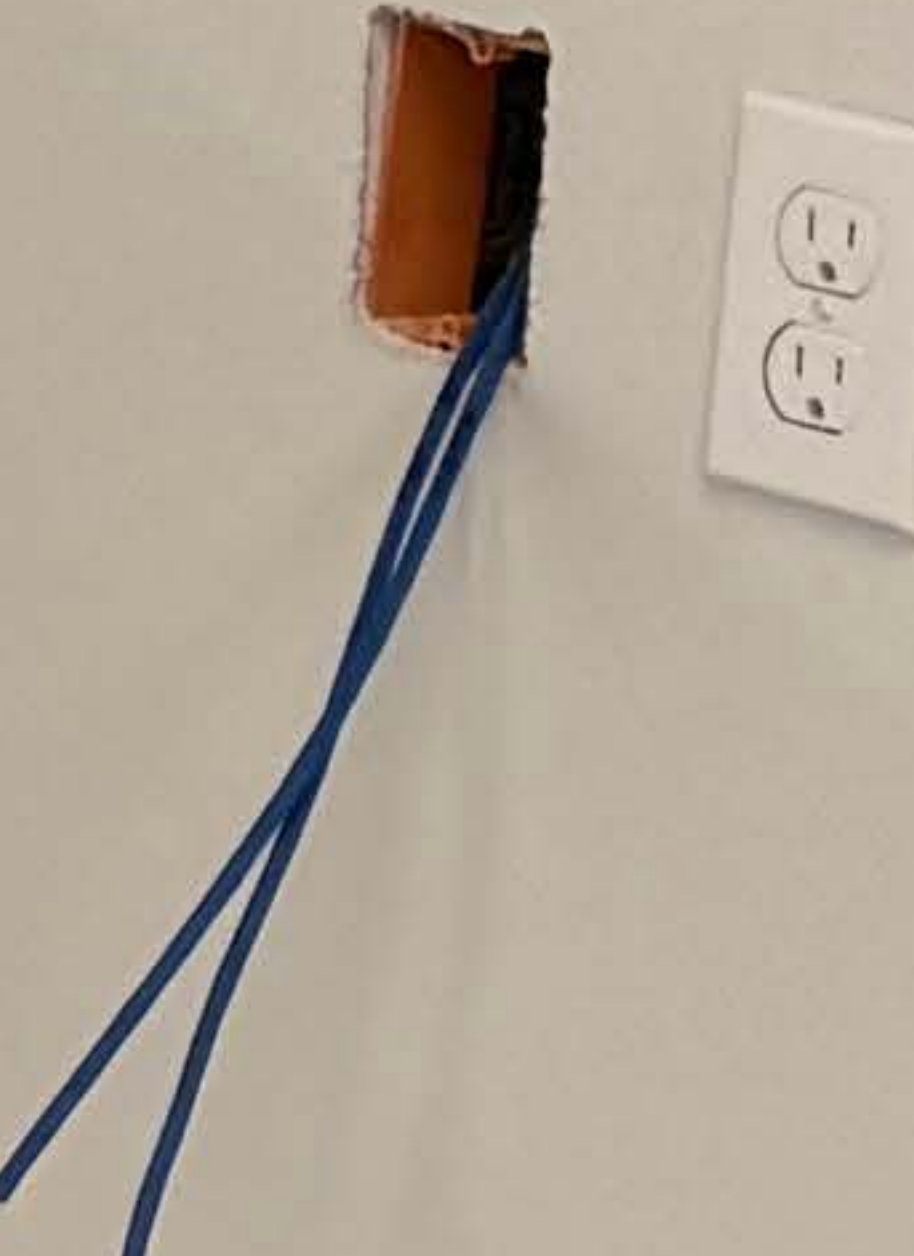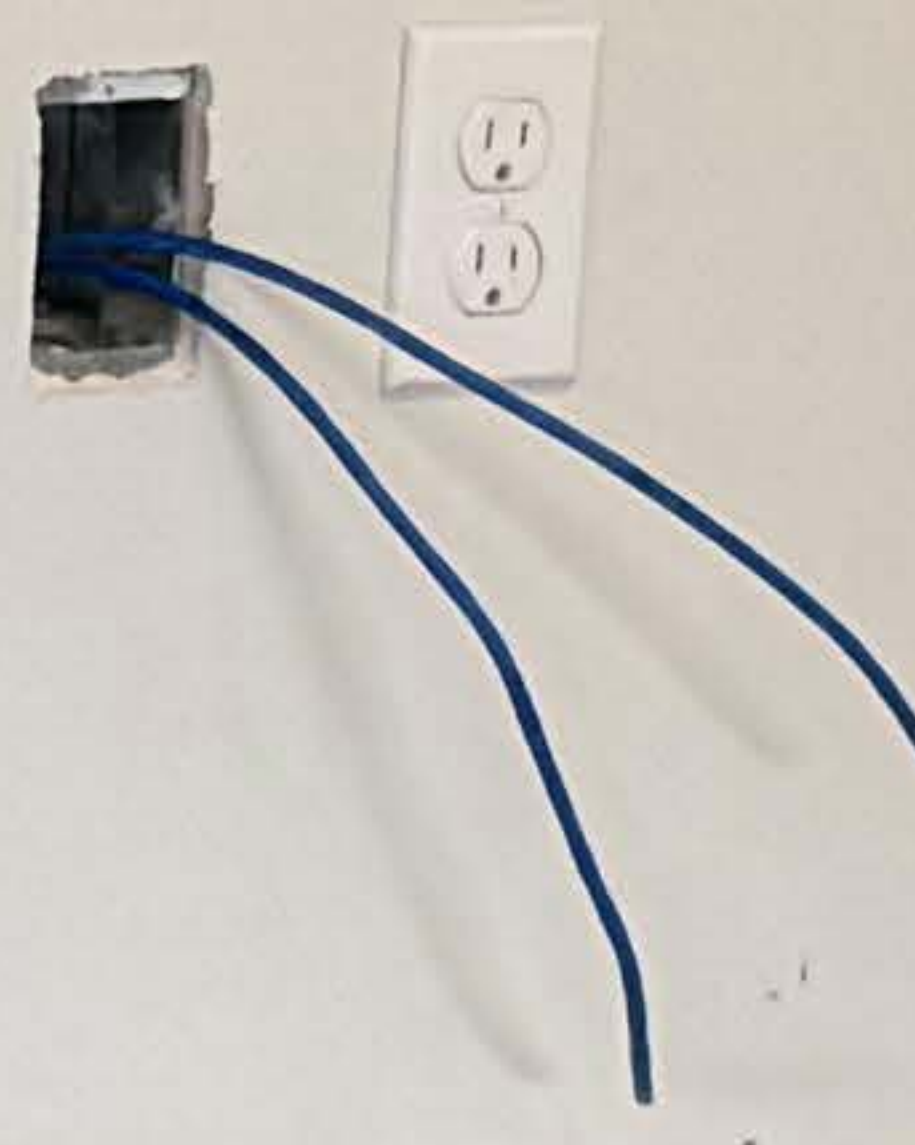

5/8" CT Type X 11/11/25 S 215232 A



Mountain Line

Departures  
TRINLINE.COM

This is an estimated time.  
Please be on the stand when your scheduled departure time.

**DANGER**  
CONSTRUCTION ZONE  
UNAUTHORIZED PERSONNEL KEEP OUT



MADE IN CHINA  
WARRANTY  
1 YEAR  
100% SATISFACTION  
GUARANTEE  
CALL 1-800-800-XXXX



DO NOT  
USE

541





